



















ID	Task Name	Duration	Start	Finish	Predecessors	20	
						Nov	Dec
1	Ottawa Landfill Contingency Plan	974 days	Tue 12/11/07	Fri 9/2/11			
2	LFG Collection System	120 days	Tue 12/11/07	Mon 5/26/08			
3	Install 18 LFG wells on slopes and top of the landfill footprint	120 days	Tue 12/11/07	Mon 5/26/08			
4	Clay Capping on slopes and top of LF	150 days	Mon 4/7/08	Fri 10/31/08			
5	Complete soil fill on the north slope	100 days	Mon 5/5/08	Fri 9/19/08			
6	Tender Capping Project	10 days	Mon 4/7/08	Fri 4/18/08			
7	Cap NE & West slopes	40 days	Mon 5/5/08	Fri 6/27/08			
8	Cap the top of the Landfill Footprint	40 days	Mon 6/30/08	Fri 8/22/08	7		
9	Cap North Slope	30 days	Mon 9/22/08	Fri 10/31/08	5		
10	Beanie Capping on top of LF	974 days	Tue 12/11/07	Fri 9/2/11			
11	Complete Beanie Cap Design	80 days	Tue 12/11/07	Mon 3/31/08			
12	Obtain C of A amendment from MOE	90 days	Tue 4/1/08	Mon 8/4/08	11		
13	Tender Beanie Cap - Phase I	10 days	Mon 5/11/09	Fri 5/22/09			
14	Install Beanie Cap - Phase I	60 days	Mon 6/15/09	Fri 9/4/09			
15	Tender Beanie Cap - Phase II	10 days	Mon 5/10/10	Fri 5/21/10			
16	Install Beanie Cap - Phase II	60 days	Mon 6/14/10	Fri 9/3/10			
17	Tender Beanie Cap - Phase III	10 days	Mon 5/9/11	Fri 5/20/11			
18	Install Beanie Cap - Phase III	60 days	Mon 6/13/11	Fri 9/2/11			
19	Air Emission Surveys Reports	736 days	Tue 4/1/08	Tue 1/25/11			
20	Conduct Survey & submit report - April 2008	20 days	Tue 4/1/08	Mon 4/28/08			
21	Post Report on WMCC website	20 days	Tue 4/29/08	Mon 5/26/08	20		
22	Conduct Survey & submit report - June 2008	20 days	Mon 6/2/08	Fri 6/27/08			
23	Post Report on WMCC website	20 days	Mon 6/30/08	Fri 7/25/08	22		
24	Conduct Survey & submit report - August 2008	20 days	Fri 8/1/08	Thu 8/28/08			
25	Post Report on WMCC website	20 days	Fri 8/29/08	Thu 9/25/08	24		
26	Conduct Survey & submit report - October 2008	20 days	Wed 10/1/08	Tue 10/28/08			
27	Post Report on WMCC website	20 days	Wed 10/29/08	Tue 11/25/08	26		
28	Conduct Survey & submit report -December 2008	20 days	Mon 12/1/08	Fri 12/26/08			
29	Post Report on WMCC website	20 days	Mon 12/29/08	Fri 1/23/09	28		
30	Conduct Survey & submit report - April 2009	20 days	Wed 4/1/09	Tue 4/28/09			
31	Post Report on WMCC website	20 days	Wed 4/29/09	Tue 5/26/09	30		
32	Conduct Survey & submit report - June 2009	20 days	Mon 6/1/09	Fri 6/26/09			
33	Post Report on WMCC website	20 days	Mon 6/29/09	Fri 7/24/09	32		
34	Conduct Survey & submit report - August 2009	20 days	Mon 8/3/09	Fri 8/28/09			
35	Post Report on WMCC website	20 days	Mon 8/31/09	Fri 9/25/09	34		
36	Conduct Survey & submit report - October 2009	20 days	Thu 10/1/09	Wed 10/28/09			
37	Post Report on WMCC website	20 days	Thu 10/29/09	Wed 11/25/09	36		
38	Conduct Survey & submit report - December 2009	20 days	Tue 12/1/09	Mon 12/28/09			
39	Post Report on WMCC website	20 days	Tue 12/29/09	Mon 1/25/10	38		




Project: Contingency plan schedule Date: Tue 12/11/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	20	
						Nov	Dec
40	Conduct Survey & submit report - April 2010	20 days	Thu 4/1/10	Wed 4/28/10			J
41	Post Report on WMCC website	20 days	Thu 4/29/10	Wed 5/26/10	40		
42	Conduct Survey & submit report - June 2010	20 days	Tue 6/1/10	Mon 6/28/10			
43	Post Report on WMCC website	20 days	Tue 6/29/10	Mon 7/26/10	42		
44	Conduct Survey & submit report - August 2010	20 days	Mon 8/2/10	Fri 8/27/10			
45	Post Report on WMCC website	20 days	Mon 8/30/10	Fri 9/24/10	44		
46	Conduct Survey & submit report - October 2010	20 days	Fri 10/1/10	Thu 10/28/10			
47	Post Report on WMCC website	20 days	Fri 10/29/10	Thu 11/25/10	46		
48	Conduct Survey & submit report - December 2010	20 days	Wed 12/1/10	Tue 12/28/10			
49	Post Report on WMCC website	20 days	Wed 12/29/10	Tue 1/25/11	48		
50	Planned Construction and/or maintenance activities report	762 days	Tue 1/1/08	Wed 12/1/10			
51	Post Report on WMCC website	1 day	Tue 1/1/08	Tue 1/1/08			
52	Post Report on WMCC website	1 day	Fri 2/1/08	Fri 2/1/08			
53	Post Report on WMCC website	1 day	Fri 2/29/08	Fri 2/29/08			
54	Post Report on WMCC website	1 day	Tue 4/1/08	Tue 4/1/08			
55	Post Report on WMCC website	1 day	Thu 5/1/08	Thu 5/1/08			
56	Post Report on WMCC website	1 day	Fri 5/30/08	Fri 5/30/08			
57	Post Report on WMCC website	1 day	Tue 7/1/08	Tue 7/1/08			
58	Post Report on WMCC website	1 day	Fri 8/1/08	Fri 8/1/08			
59	Post Report on WMCC website	1 day	Mon 9/1/08	Mon 9/1/08			
60	Post Report on WMCC website	1 day	Wed 10/1/08	Wed 10/1/08			
61	Post Report on WMCC website	1 day	Fri 10/31/08	Fri 10/31/08			
62	Post Report on WMCC website	1 day	Mon 12/1/08	Mon 12/1/08			
63	Post Report on WMCC website	1 day	Thu 1/1/09	Thu 1/1/09			
64	Post Report on WMCC website	1 day	Fri 1/30/09	Fri 1/30/09			
65	Post Report on WMCC website	1 day	Fri 2/27/09	Fri 2/27/09			
66	Post Report on WMCC website	1 day	Wed 4/1/09	Wed 4/1/09			
67	Post Report on WMCC website	1 day	Fri 5/1/09	Fri 5/1/09			
68	Post Report on WMCC website	1 day	Mon 6/1/09	Mon 6/1/09			
69	Post Report on WMCC website	1 day	Wed 7/1/09	Wed 7/1/09			
70	Post Report on WMCC website	1 day	Fri 7/31/09	Fri 7/31/09			
71	Post Report on WMCC website	1 day	Tue 9/1/09	Tue 9/1/09			
72	Post Report on WMCC website	1 day	Thu 10/1/09	Thu 10/1/09			
73	Post Report on WMCC website	1 day	Fri 10/30/09	Fri 10/30/09			
74	Post Report on WMCC website	1 day	Tue 12/1/09	Tue 12/1/09			
75	Post Report on WMCC website	1 day	Fri 1/1/10	Fri 1/1/10			
76	Post Report on WMCC website	1 day	Mon 2/1/10	Mon 2/1/10			
77	Post Report on WMCC website	1 day	Mon 3/1/10	Mon 3/1/10			
78	Post Report on WMCC website	1 day	Thu 4/1/10	Thu 4/1/10			

Project: Contingency plan schedule Date: Tue 12/11/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


ID	Task Name	Duration	Start	Finish	Predecessors	20		
						Nov	Dec	J
79	Post Report on WMCC website	1 day	Fri 4/30/10	Fri 4/30/10				
80	Post Report on WMCC website	1 day	Tue 6/1/10	Tue 6/1/10				
81	Post Report on WMCC website	1 day	Thu 7/1/10	Thu 7/1/10				
82	Post Report on WMCC website	1 day	Fri 7/30/10	Fri 7/30/10				
83	Post Report on WMCC website	1 day	Wed 9/1/10	Wed 9/1/10				
84	Post Report on WMCC website	1 day	Fri 10/1/10	Fri 10/1/10				
85	Post Report on WMCC website	1 day	Mon 11/1/10	Mon 11/1/10				
86	Post Report on WMCC website	1 day	Wed 12/1/10	Wed 12/1/10				

Project: Contingency plan schedule Date: Tue 12/11/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

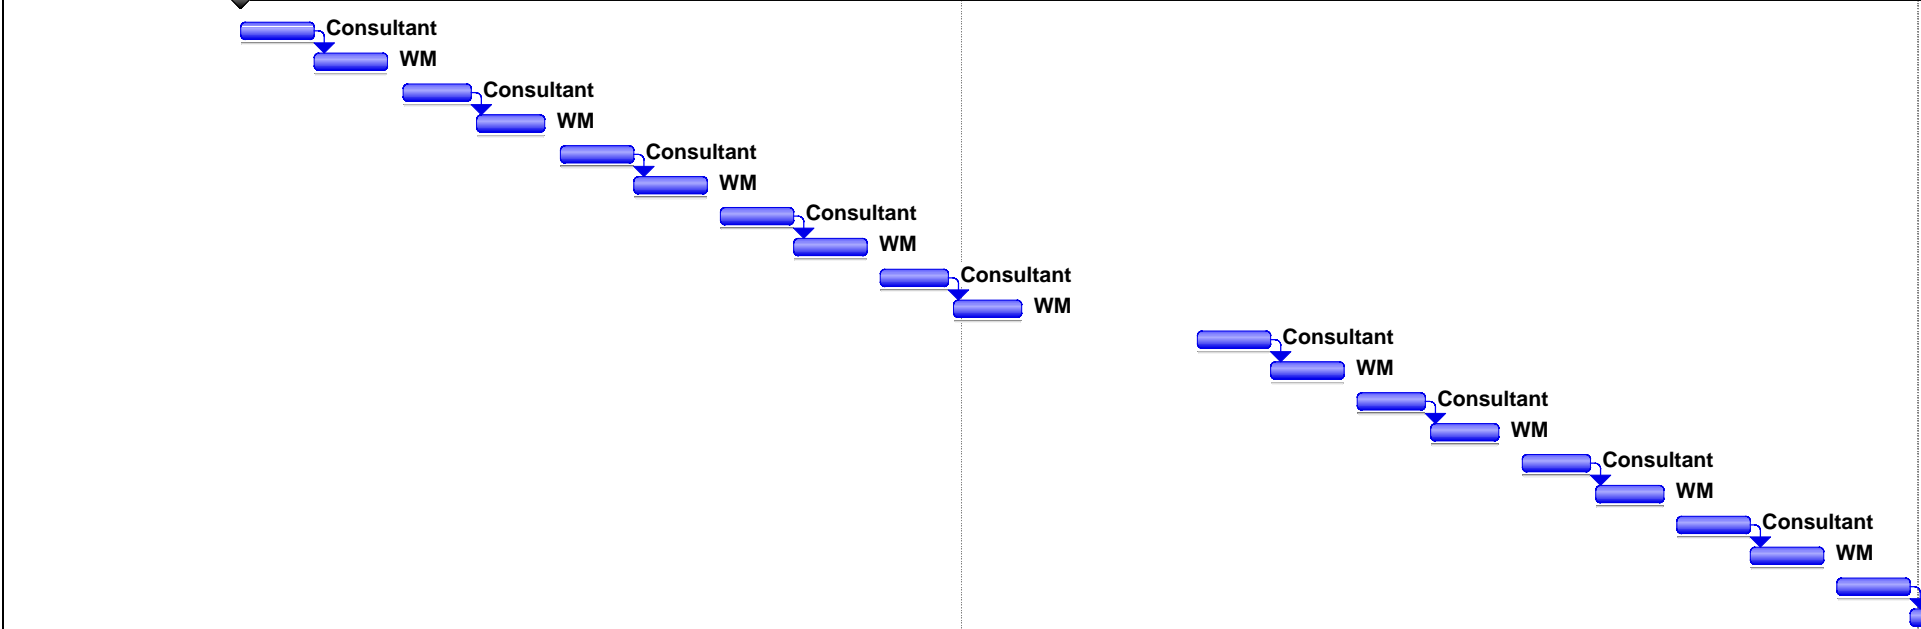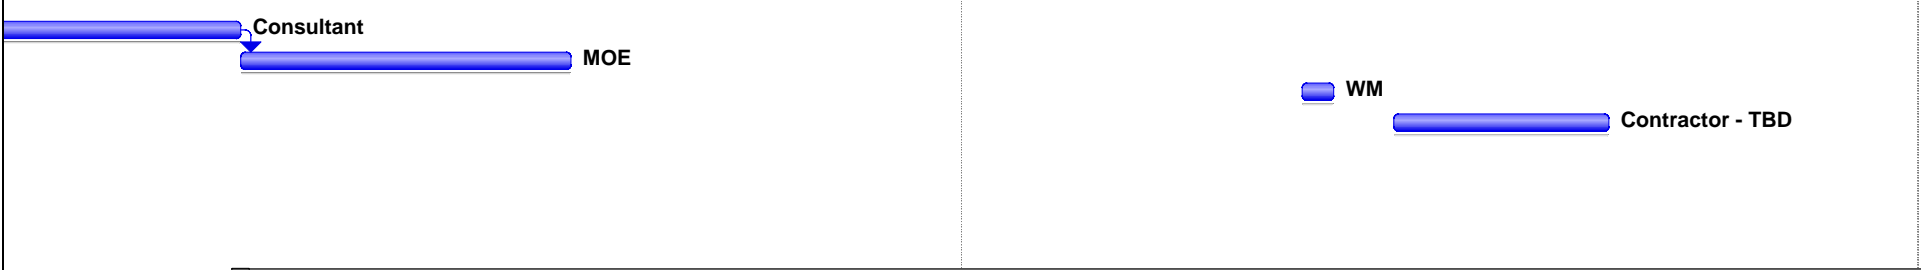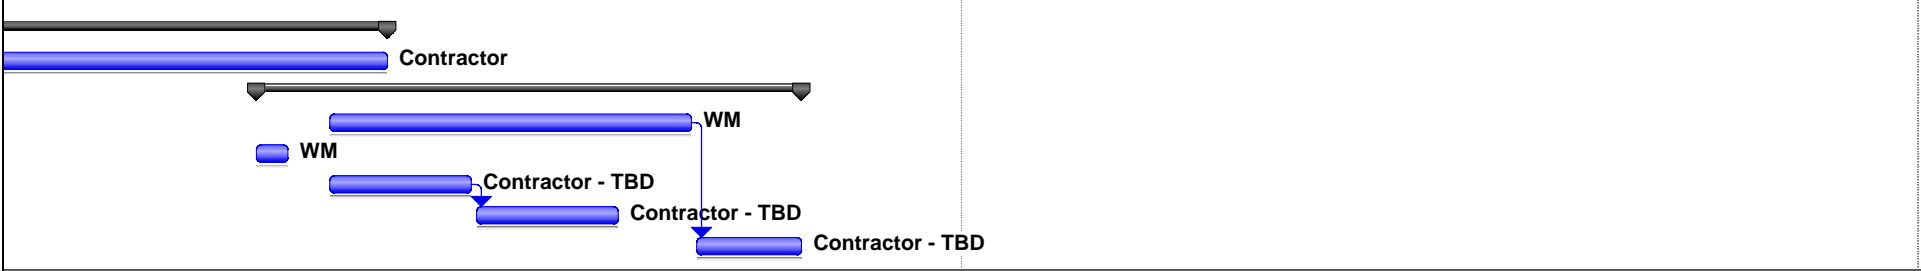





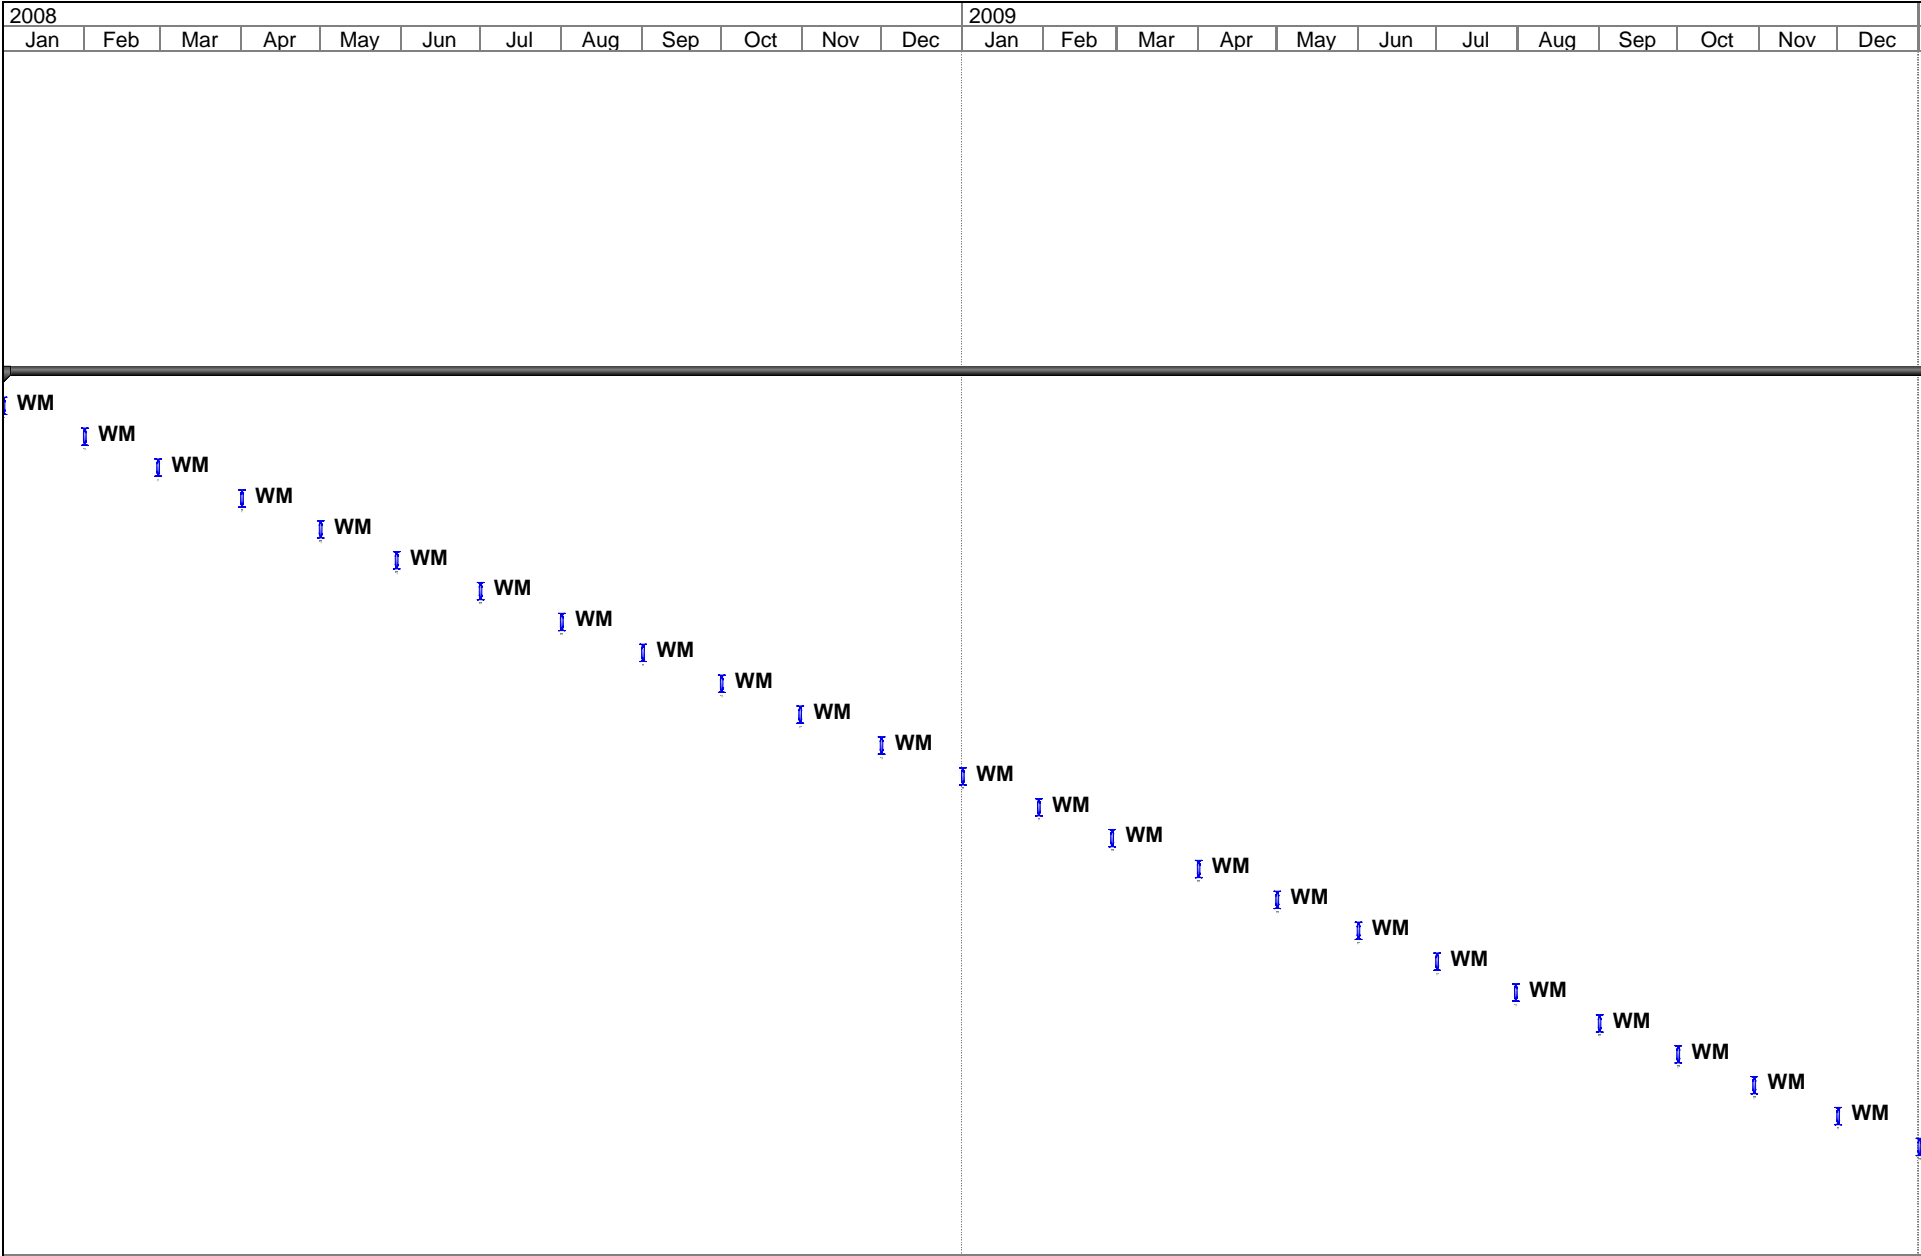




Project: Contingency plan schedule
Date: Tue 12/11/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	












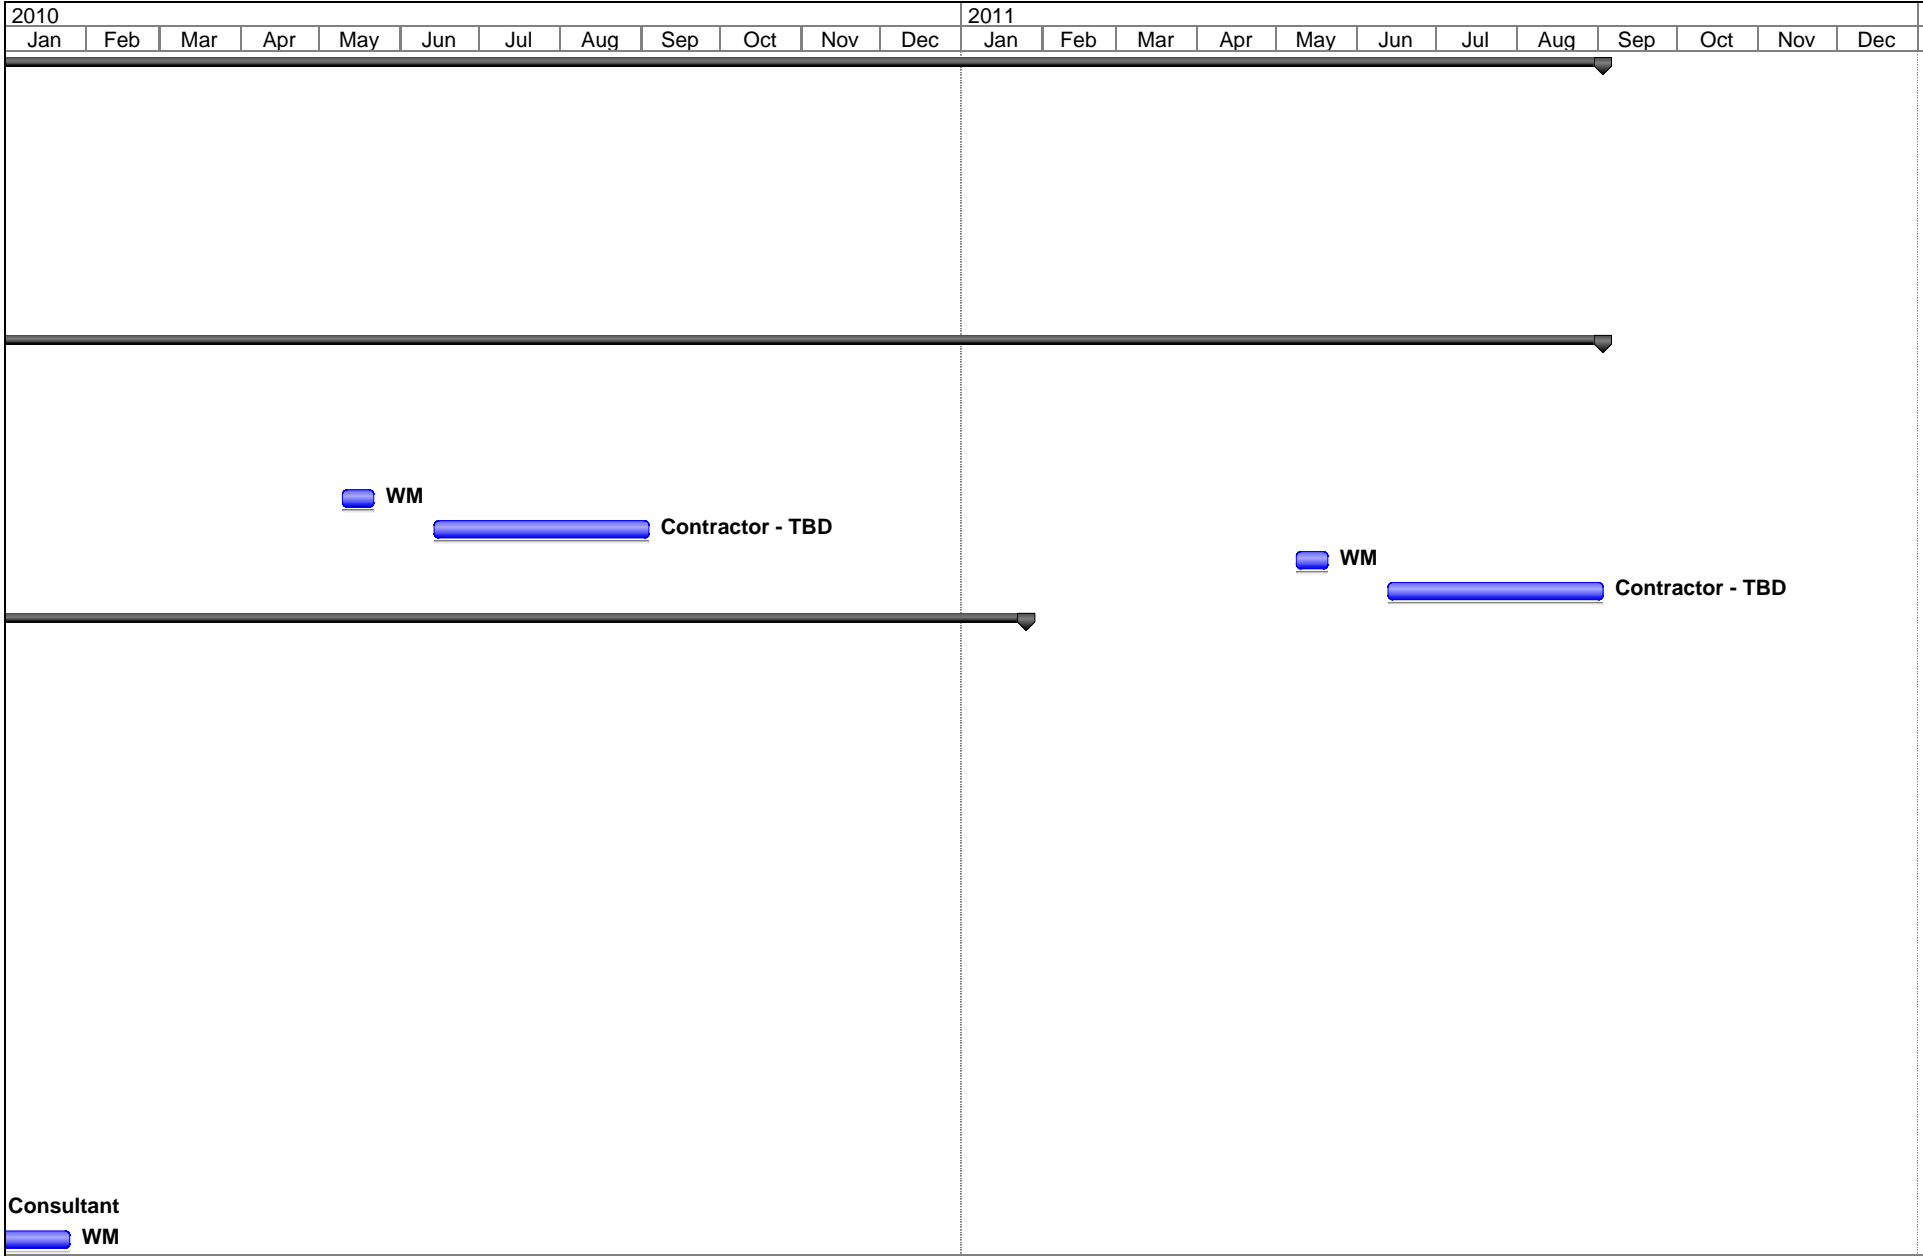
Project: Contingency plan schedule
 Date: Tue 12/11/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

2008												2009											
Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec

Project: Contingency plan schedule
Date: Tue 12/11/07


Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	



Consultant


WM

Project: Contingency plan schedule Date: Tue 12/11/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

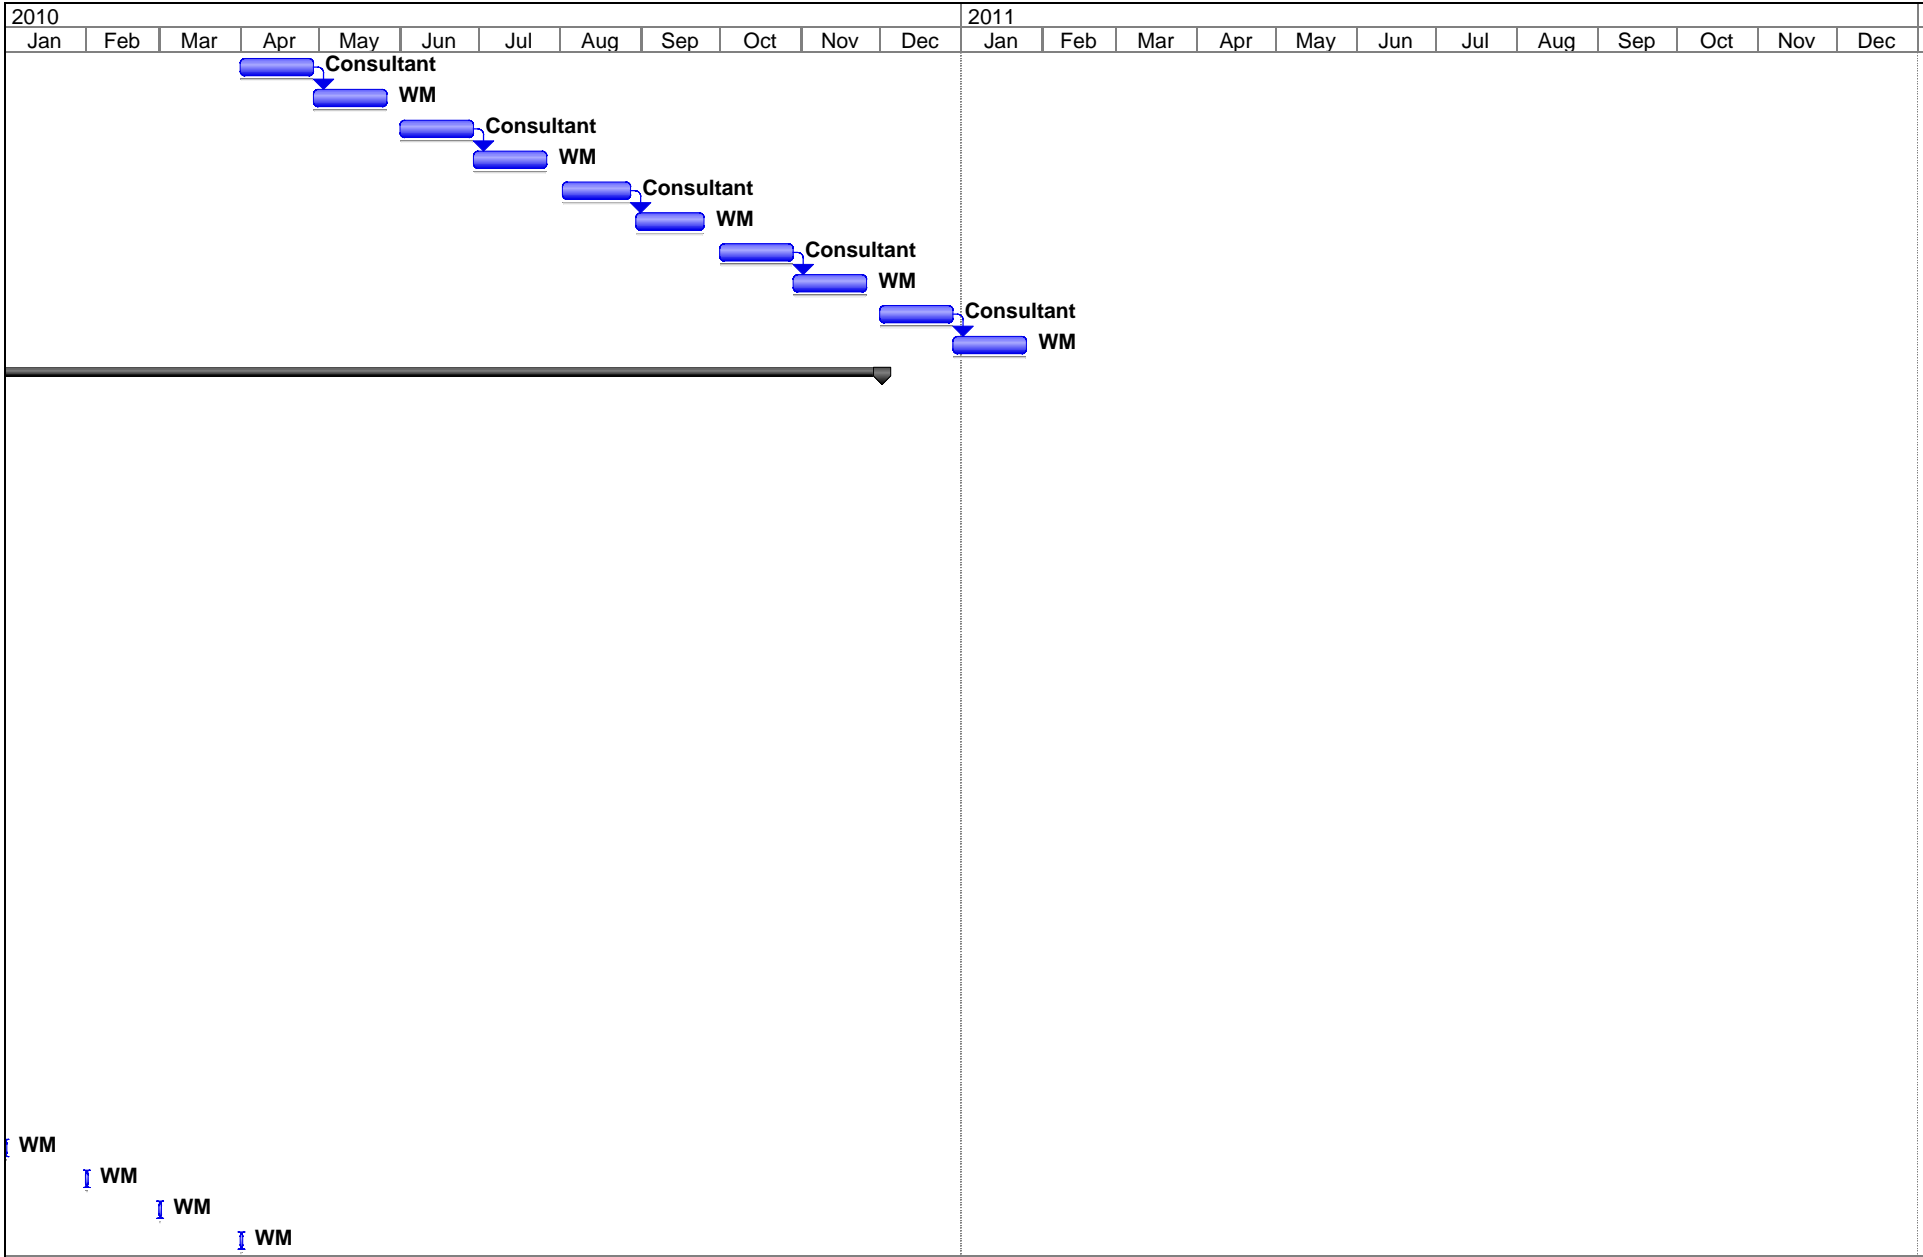





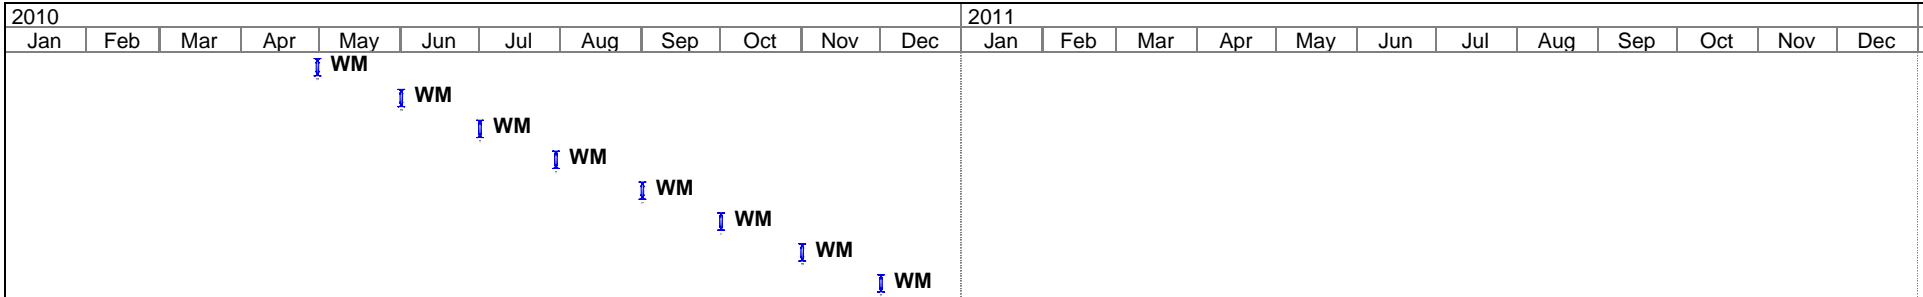



WM
WM
WM
WM

Project: Contingency plan schedule Date: Tue 12/11/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Contingency plan schedule
 Date: Tue 12/11/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
